


Semester 1 Deliverables - COMP2002:

- State of Play:

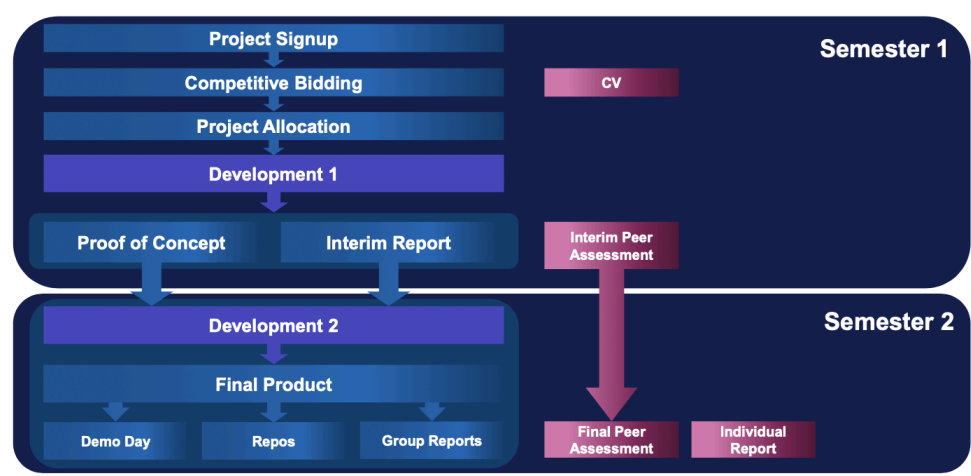

- Project Allocation:

- You should be in contact with your supervisor / sponsor:

- Set up recurring meetings with your academic supervisor.
- **Every** team member is expected in each meeting.
- **Every** team member should contribute equally to these meetings.

- Development 1 - Expectations:

- Implement of an initial prototype

- Demonstrate that architecture and methods / approaches work.

- Teams lead the project:

- Expected to use SCRUM process (Trello, stack, sprints, backlogs)
- Document your process (story point graph)
- Supervisors provided guidance.

- You are expected to use Git.

- Deliverables:

- Admin:

- NDAs,
- Preliminary ethics checklist (Administrator)

- Semester 1 Deliverables:

- Interim report (underpins development 2 and final report - rubric)
- Document your progression - story point graphs.
- Git repository (& demo)
- Interim peer review

- Semester 2 Deliverables:

- Individual reports & peer review,
- Final group reports & Demonstration,
- Code repository,

		Criteria	Mark Weight	Awarded Mark (out of 100)
Interim Report	Project Background & Understanding (10%)	Criteria: - Evidence of understanding of the initial brief / specification. - Evidence of own interpretations / additions / innovations . - Depth and context of the problem presented (e.g. existing products).	10%	
	Requirements & Critical Analysis (15%)	Criteria: - Depth / clarity / coverage and appropriate prioritisation of requirements . - Motivation / reflection for changes to requirements and scope reductions. - Results of focus groups / user surveys (where applicable). - Analysis of hardware / tools / methods / software libraries for the project.	15%	
	Initial software implementation & testing (30%)	Criteria: - Data storage / management / manipulation / use of (personal) data (if applicable). - Architecture / design / proof of concept of the prototype. - Appropriate use of version control system (branching / merging). - Evidence of testing . - Preliminary inline software documentation .	30%	
	Project Management & progress (15%)	Criteria: - Evidence of effective / appropriate project management (Agile, SCRUM, SCRUMBAN, Kanban, etc.). - Documentation of sprints / retrospectives / workload management / formal meetings (where applicable). - Use of project management tools (Trello / Microsoft Planner / Teams / Slack). - Effective use of team skills / skills transfers / cross training. - Professional attitude / disciplined / consistent / timely / punctual / autonomous & self organising .	15%	
	Preliminary Reflection (15%)	Criteria: - Tools / techniques / methods / technical difficulties / testing . - On project management / current progress . - Functioning of the team so far. - Forward plan / address concerns identified.	15%	
	Style (8%)	Criteria: - Accessibility / clarity & motivation of the argument / structure (e.g. by key parts / components of the project) - Concise / conceptual descriptions / appropriately balanced content / length / depth - Grammar / spelling / articulation / formatting / structure / jargon & definitions - Use of visuals / graphics	8%	
	Resource links (2%)	Criteria: - Links to document repository / project management documentation (e.g. Trello / Microsoft Planner) / code repository	2%	
	Conclusion & Summary (5%)	Criteria: - summary of key points and future plan	5%	
Total:				

- Mark Scaling:

-

Group Deliverable	Component Contribution	Overall Contribution
Eol & Pitch	15%	12%
Interim Report	10%	8%
Interim Peer Assessment	-	-
Group Report	25%	20%
Stand / Demo / Presentation	15%	12%
Software / Project Management	35%	28%

Individual Deliverable	Component Contribution	Overall Contribution
CV	20%	4%
Peer Assessment	20%	4%
Individual Report	60%	12%

- Assessment Scaling:

- Assessment considers:

- Group elements (80%)
- Individual elements (20%)

- Group elements are scaled based on:

- Individual reports,
- Group deliverables (docs and code repository)
- Peer assessment (deviation from average)
- Supervisor moderation.

- SCRUM:

- SCRUM Project Characteristics:

- Complicated & complex projects with technical unknown
- Emerging & evolving requirements
- Small teams
- Uncertainty

- SCRUM - Overview:

- Three roles:

- Product owner - has 'vision', knows the business needs (sponsor/supervisor)
- SCRUM coach - manages process (team lead)
- Dev team.

- Three artifacts:

- Backlog - user stories, bugs, tasks (product vision)
- Sprint backlog - items for next sprint/increment
- Product,

- Four timeboxed meetings:

- Sprint planning - shortlist priority user stores for the next sprint.
- 'Daily' Standup (SCRUM) - achieved, plan, impediments
- Sprint review - results & demo with stakeholders
- Retrospective - went well, improvements, changes (teams)

- Artifacts - Backlog(s)

- Product backlog:

- **User story:** "As a [role], I want [capability], so that I can [benefit]"
 - Detail added in conversations
 - Acceptance criteria
 - Size – story points
- **Tasks:** items that provide indirect value to the project
- **Bugs:** continuous debugging

- Sprint backlog:

- Contains items from the product backlog to address in the next increment

- Meetings - Sprint Planning:

- Should consider:

- Capacity Planning - Member availability, coursework
- Select user stories for next increments
- Breaks down user stories into tasks,
- Estimate the story points per tasks,
- Defines overall sprint goal.

- Should not exceed 1h for 2 weeks sprints.

- **Team decides on items to include, and sets short term goals.**
- **Results in a total number of story points to include.**

- SCRUM - Timings:

- Concepts:

- Story points - estimation of the time required to complete a feature
- Velocity - #story points per sprint.
- Burndown - average velocity per sprint.

- Tools:

- Jira, Azure, Trello, MS Planner
- Generate predictions on completion dates and analyse.
- What-if analysis (e.g., when adding additional features)

- Meetings - Stand-Ups (SCRUMs)

- No less than twice per week (normally daily, can be online)

- For every member:

- What have you done since the last scrum?
- What are you committing to getting done before the scrum?
- What impediments are holding you back?

- Time boxed to 15 minutes (followed by an off-line discussion)

- Review of the burndown chart.

- Sprint Review:

- Constructive discussion with stakeholders (sponsor/supervisor)

- What was the goal of the sprint
- What items were completed
- What successes and problems
- Product demonstration (demonstrable increment)

- Discussion of future plan

- Discussion of timeline.

- Retrospective:

- Discussion between team members and supervisors

- What went well
- What could have gone better
- what can be improved/trialed

- Teamwork - Communication:

- Balanced 'talking':

- Everyone talks an equal amount of time (keep contributions short)

- Face-to-Face when possible:

- Better response if you ask someone something in person

- Communicate Frequently.

- Advice:

- Have regular meetings with your supervisors / sponsors:

- No less than once every 14 days (set up recurring meeting)
- Academic and industry (if applicable)

- Start writing early

- Group / individual reports
- Peer assessment

- Follow a SCRUM process:

- Backlog => sprint planning => sprint backlog => stand-ups => sprint review => retrospective => repeat
- Demo after every sprint

- The process and deliverables are marked

- Final Goal - Showcase Day:

- Consists of:
 - Formal presentation (20 minutes)
 - Guest speakers,
 - Free flow demo's
- Prizes for best overall projects,
- Runner ups,
- Best demo,

- Eol feedback:

- Eol feedback for the bids (Eols and patches) will be made available on

Moodle:

- Team administrators - please share this with the team.
- The marks on Moodle will be the average for all three bids:**
 - **50%** for the Eols,
 - **50%** for the Pitches (Videos & Q&A)
- Remember - if there is anything you think I should be aware of - please contact.
